Approved For Release 2006/04/13 : CIA-RDP67B00511R000100180024-6

SCHEDULE FOR SYSTEMS #1 AND 2

JULY 6, 1962

SYSTEM	OPERATION	JUL	AUG	SEP	OCT	NOV	DEC	JAN '63	FEB	MAR	APR	MAY	JUN
PROTOTYPE (SYSTEM #1)	ASSEMBLY												
	FINAL WIRING												
	OPERATE SYSTEM												
	OPERATE STABILIZATION												
	OPERATE COMPLETE SYS.												
	PHASE SCANNERS												
	FLT. TEST INSTALLATION												
	LOCAL FLIGHT TEST												
	INSTRUMENT C-123												
	GIMBAL TEST												
	FLIGHT TEST #1												
	DOWNTIME												
	FLIGHT TEST #2												
	DOWNTIME												
	FLIGHT TEST #3												
	DATA REDUCTION												
	TEST IN AREA												
SYSTEM #2	PROCUREMENT (FRAME, PLATFORM PARTS)												
	ELECTRONIC SUBASSEMBLY												
	FILM TRANSPORT												
	ASSEMBLY TO PLATFORM												
	PLATFORM SUBASSEMBLIES												
	OPTICS (ASSY, ALIGN. & FOCUS)												
	IN HOUSE TEST												
	TEST AT AREA												

Approved For Release 2006/04/13 : CIA-RDP67B00511R000100180024-6

Approved For Release 2006/04/13 : CIA-RDP67B00511R000100180024-6

Office File Info & E

Schedule presented on 8 May 62

"Unacceptable"

PROGRAM SCHEDULE

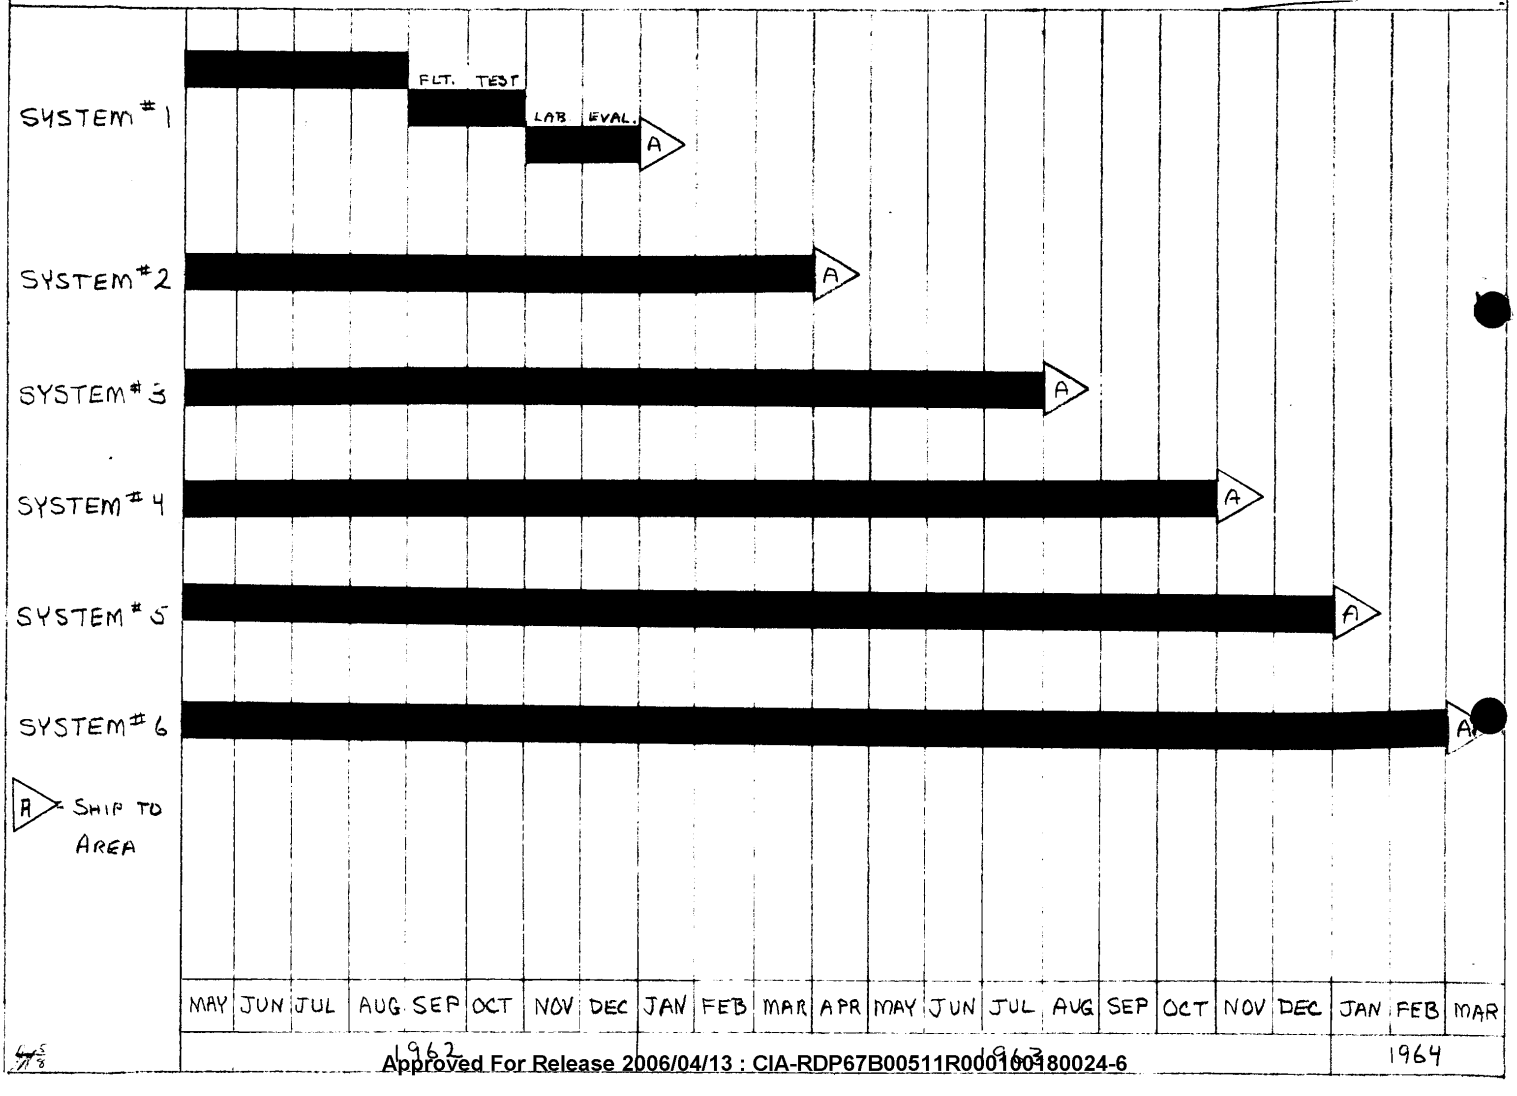

Approved For Release 2006/04/13 : CIA-RDP67B00511R000100180024-6
